

LA-UR-12-22874

Approved for public release; distribution is unlimited.

Title: LANL 3706 TRU Campaign Status Report - FY12 3rd Quarter

Author(s): Jones, Patricia

Intended for: Posting on website
Web



Disclaimer:

Los Alamos National Laboratory, an affirmative action/equal opportunity employer, is operated by the Los Alamos National Security, LLC for the National Nuclear Security Administration of the U.S. Department of Energy under contract DE-AC52-06NA25396. By approving this article, the publisher recognizes that the U.S. Government retains nonexclusive, royalty-free license to publish or reproduce the published form of this contribution, or to allow others to do so, for U.S. Government purposes. Los Alamos National Laboratory requests that the publisher identify this article as work performed under the auspices of the U.S. Department of Energy. Los Alamos National Laboratory strongly supports academic freedom and a researcher's right to publish; as an institution, however, the Laboratory does not endorse the viewpoint of a publication or guarantee its technical correctness.

LANL 3,706 TRU Campaign Status Report – FY12 3rd Qtr. (April thru June 2012)

Processing Highlights

RANT (Shipping Facility):

- During single shift operation, shipped 62 shipments for a cumulative total of 150 shipments to WIPP in FY12 with a FY goal of 184 shipments.
- Began installation of a Mobile Loading Unit for system redundancy.
- Began construction on the RANT Transportation Center to support FY13 shipment ramp-up.

WCRRF (High Activity Drum Line):

- During split shift operation, the repackaging line performed remediation on 226 drum equivalents (DE), for a total of 547 DE since the beginning of the campaign.

Building 412 (Box Line):

- During single and split shift operation, the repackaging line performed remediation on 125 m3, for a total of 264 m3 since the beginning of the campaign.

- Multiple shifts allow for crew development & training in preparation for new box lines.

Dome 231 (Drums):

- Maintain schedule to complete conversion to Box Line readiness in August, 2012 with scheduled start-up in September, 2012.

Dome 375 (Large Box Line):

- Continues process capability construction (conversion to large box line) and is scheduled to be in operation on September, 2012.


Central Characterization Project:

- Drum Venting System (DVS) operations started.
- As of June 30, 313 containers are approved in the Waste Disposal System database, and 663 are awaiting approval.


TRU Volume Removed		FY12 thru 07/01/12			PROJECTIONS FOR NEXT QUARTER *			
SHIPMENTS * (as of 07/01/12)		June 2014 Goal	Q3 Actual to Date	Cumulative Actual to Date	% Complete	End of 4th Qtr.	Cumulative by End of Qtr.	Cum. % Complete
3,706 TRU Campaign	Volume (m3)	3706.0	339.3	584.7	15.8%	403.9	800.0	22%
	Drum Equivalents	17817.3	1631.1	2811.2		1941.8	3846.2	
	Radioactivity (PE Ci)	41510.7	3357.5	12694.8	31%	9914.3	22500.0	54%

3,706 LANL TRU Campaign Performance


(Target = 3,706 m3; Remaining = 3,121 m3)

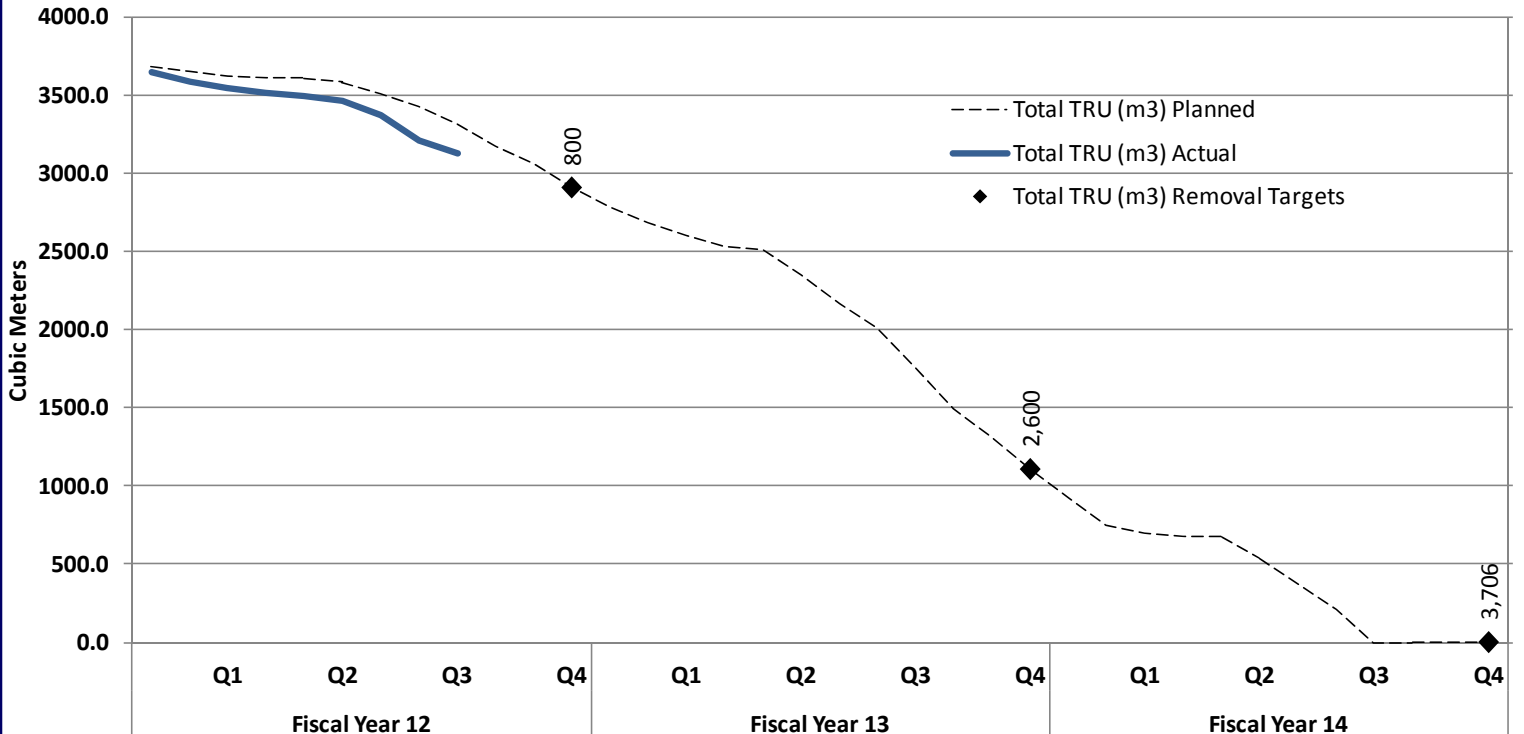


Parent vs. Shipped Volumes

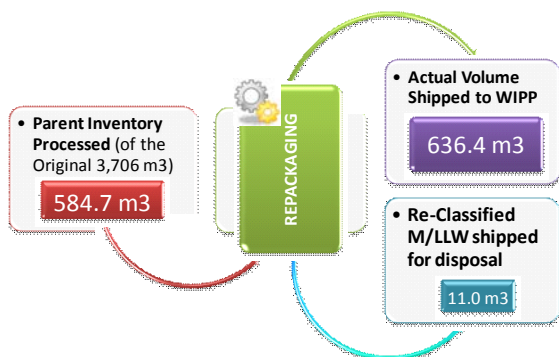


**MAR Removal - Total Campaign

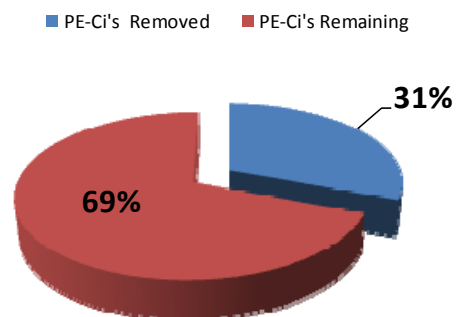

3,706 Goal vs. Progress (Volumes)

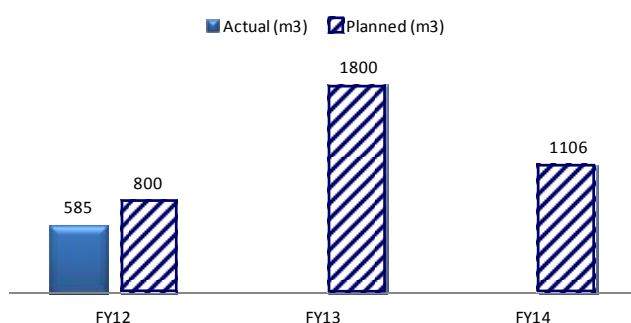

3,706 TRU Campaign Shipment Progress *

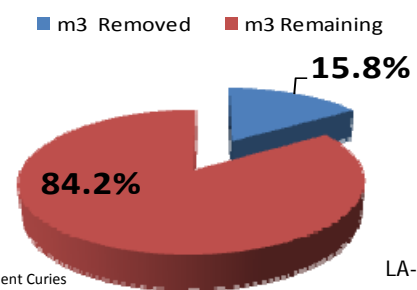

* = Parent Volume
** - Material at Risk
PE-Ci = Plutonium Equivalent Curies
